
CCNA-12 | Secure Campus Segmentation and Access Control for FIDS | Schedule and Time Management


Project Manager: Carl Edouard Sponsor: Fairmont Integrated Defense Solutions Built on the eight week WBS in Appendix B of the signed scope, tracked in Jira as five sprints

Start	Baseline finish (signed scope)	Forecast finish	Course deadline	Total duration (days)	Buffer left before deadline (days)	Tasks complete
Sep 29	Nov 21	Dec 1	Dec 5	64	3	10 of 40

WBS	Activity	Owner	Start	Finish	Days	Depends on	Status	Type	Baseline start	Baseline finish	Slip (days)
S1	SPRINT 1 (Jira)	All	Sep 29	Oct 10	12		Complete	Sprint			
W1	WEEK 1 Understand the job and lay the foundation	All	Sep 29	Oct 3	5		Complete	Week	Sep 29	Oct 3	0
1.1	Read the scope, list every requirement, and log questions for the sponsor	Carl	Sep 29	Sep 30	2		Complete	Task			
1.2	Study the core skills in NetAcad: VLANs, OSPF routing and ACL rules (SRWE 3 and 4, ENSA 1 to 4)	All	Sep 29	Oct 3	5		Complete	Task			
1.3	Draw the physical layout: where each router and switch sits, which zone joins which OSPF area, how it is all cabled	Devam	Sep 30	Oct 2	3	1.1	Complete	Task			
1.4	Agree on one naming system for devices and port descriptions so every config reads the same way	Carl, Devam	Oct 1	Oct 2	2	1.3	Complete	Task			
1.5	Create the GitHub repository; all four members commit the starting topology	Carl	Sep 30	Oct 3	4		Complete	Task			
1.6	Set up the Jira board with five sprints to track the work	Carl	Oct 1	Oct 3	3		Complete	Task			
G1	GATE Layout and naming agreed by all four, everyone committing to GitHub	Carl	Oct 3	Oct 3	1	1.3, 1.4, 1.5	Complete	Gate			
W2	WEEK 2 Plan every address and every rule on paper before touching a device	Jaden, Carl	Oct 6	Oct 17	12	G1	In progress	Week	Oct 6	Oct 10	7
2.1	Addressing plan (VLSM): size each zone's IP range so the whole zone can be advertised as one summary route at its border router	Jaden	Oct 6	Oct 13	8	G1	Complete	Task			
2.2	Map each VLAN to its OSPF area and write down why	Jaden, Carl	Oct 7	Oct 13	7	2.1	Complete	Task			
2.3	Policy matrix: for every pair of zones, in each direction, decide allow or block and record the reason	Jaden, Michael	Oct 8	Oct 13	6	2.1	Complete	Task			
2.4	Give each router a fixed router ID and map the path traffic should take between zones	Carl	Oct 8	Oct 13	6	2.2	Complete	Task			
2.5	Sponsor acknowledges the scope on Discord	Carl	Oct 8	Oct 8	1		Complete	Gate			
2.6	PM Readiness Package submitted on Canvas	Carl	Oct 13	Oct 13	1	2.5	Complete	Gate			
2.7	PM approves the addressing plan, then sends the plan and matrix to Thompson	Carl	Oct 15	Oct 15	1	2.1, 2.3, 2.5	Not started	Task			
G2	GATE SPONSOR DESIGN REVIEW: Thompson approves the plan and matrix. Nothing is configured before this.	Carl	Oct 17	Oct 17	1	2.7	Replanned	Gate			
S2	SPRINT 2 (Jira)	All	Oct 13	Oct 24	12	G1	In progress	Sprint			
W3	WEEK 3 Build the backbone and the zones, with no blocking yet	All	Oct 13	Oct 24	12	2.4	In progress	Week	Oct 13	Oct 17	7
3.0	Prep during the review: place and cable every device in Packet Tracer, write each config as a text file ready to paste	All	Oct 13	Oct 17	5	2.4	In progress	Task			
3.1	Bring up the management backbone and OSPF routing across all areas, using the fixed router IDs	Carl	Oct 20	Oct 22	3	G2, 3.0	Not started	Task			
3.2	Create each zone's VLANs, link switches with 802.1Q trunks, and turn on routing between VLANs	Jaden, Michael, Devam	Oct 20	Oct 23	4	G2, 3.0	Not started	Task			
3.3	Ping test inside every zone and save proof that the routers became OSPF neighbors	Michael	Oct 22	Oct 23	2	3.1, 3.2	Not started	Task			
3.4	Confirm each border router advertises its zone as one summary route, matching the Week 2 plan	Jaden	Oct 23	Oct 23	1	3.1	Not started	Task			
3.5	Save a before snapshot of traffic so the effect of the ACLs can be shown later	Devam	Oct 23	Oct 24	2	3.3	Not started	Task			
G3	GATE All OSPF neighbors FULL, every zone reaches itself, summary routes visible, no ACLs yet	Carl	Oct 24	Oct 24	1	3.3, 3.4, 3.5	Not started	Gate			
S3	SPRINT 3 (Jira)	All	Oct 27	Nov 7	12	G3	Not started	Sprint			
W4	WEEK 4 Turn on the rules between zones (ACLs)	Jaden	Oct 27	Oct 31	5	G3	Not started	Week	Oct 20	Oct 24	7
4.1	Write extended ACLs for every zone border, check each line against the matrix, then apply them	Jaden	Oct 27	Oct 29	3	G3	Not started	Task			
4.2	DMZ rules by service: allow only the named services on each server, block every other port	Devam, Jaden	Oct 28	Oct 30	3	4.1	Not started	Task			
4.3	Test allowed traffic first, then confirm blocked traffic is actually blocked	Michael	Oct 29	Oct 30	2	4.1	Not started	Task			
4.4	Capture ACL hit counters before and after each test; confirm Contractor/Guest reaches nothing internal	Michael	Oct 30	Oct 31	2	4.3	Not started	Task			
G4	GATE Every rule does what the matrix says, and hit counters prove it	Jaden	Oct 31	Oct 31	1	4.2, 4.4	Not started	Gate			
W5	WEEK 5 Test every zone pair and train on each other's zones	Michael	Nov 3	Nov 7	5	G4	Not started	Week	Oct 27	Oct 31	7
5.1	Test every pair of zones in both directions and save proof for each one	Michael, All	Nov 3	Nov 5	3	G4	Not started	Task			
5.2	Turn on logging for key block rules and capture a blocked attempt as it happens	Michael	Nov 4	Nov 5	2	G4	Not started	Task			
5.3	Fix any zone pair that does not behave the way the matrix says it should	Jaden	Nov 5	Nov 6	2	5.1	Not started	Task			
5.4	Cross training: each member finds and fixes a fault planted in someone else's zone	All	Nov 6	Nov 7	2	5.1	Not started	Task			
G5	GATE Every zone pair proven; every member has fixed a fault outside their own zone	Michael	Nov 7	Nov 7	1	5.3, 5.4	Not started	Gate			

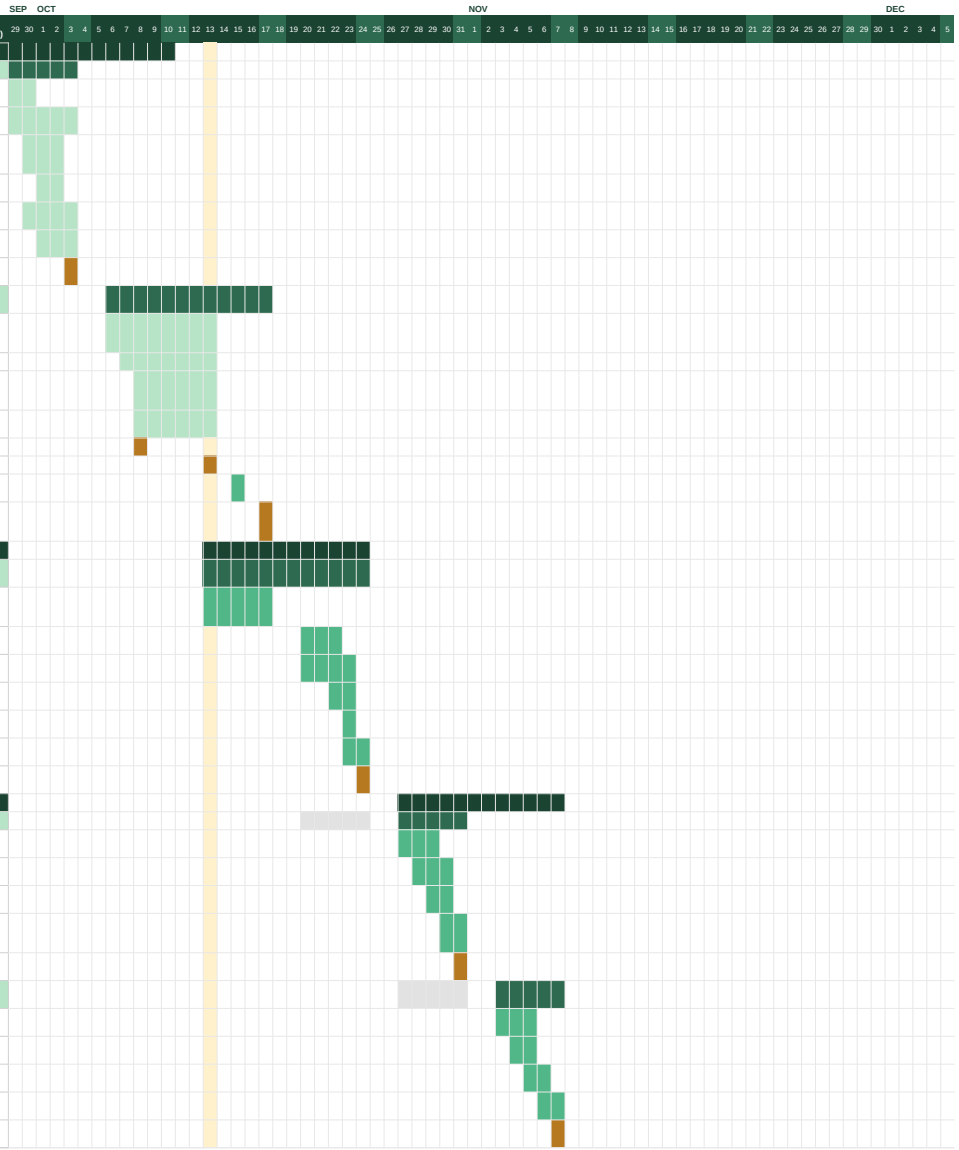

S4	SPRINT 4 (Jira)	All	Nov 10	Nov 21	12	G5	Not started	Sprint			
W6	WEEK 6 Lock it down, then break it on purpose	Carl, Devam	Nov 10	Nov 14	5	G5	Not started	Week	Nov 3	Nov 7	7
6.1	Harden device access on every router and switch so only authorized admins can log in	Devam	Nov 10	Nov 11	2	G5	Not started	Task			
6.2	OSPF authentication on backbone links so only trusted routers share routes; user facing ports set passive	Carl	Nov 10	Nov 11	2	G5	Not started	Task			
6.3	Cut a zone link on purpose and time how long OSPF takes to find a new path	Michael, Carl	Nov 12	Nov 13	2	6.2	Not started	Task			
6.4	Remove a border ACL and put it back, confirming nothing slips through in between	Jaden	Nov 12	Nov 13	2	6.1	Not started	Task			
6.5	After rerouting, recheck a sample of zone pairs to prove the rules still hold	Michael	Nov 13	Nov 14	2	6.3	Not started	Task			
G6	GATE Hardening done, every failure test run once, rules still enforced afterward	Carl	Nov 14	Nov 14	1	6.4, 6.5	Not started	Gate			
W7	WEEK 7 Run every test three times and write it all down	Michael, Devam	Nov 17	Nov 21	5	G6	Not started	Week	Nov 10	Nov 14	7
7.1	Run every acceptance test; anything timed gets three runs	Michael, All	Nov 17	Nov 19	3	G6	Not started	Task			
7.2	Record backup paths and recovery times with timestamps	Michael	Nov 18	Nov 19	2	7.1	Not started	Task			
7.3	Export every device config and add notes explaining any choice that is not obvious	Devam, All	Nov 18	Nov 20	3	G6	Not started	Task			
7.4	Finish the logical and physical diagrams so they match the real build	Devam	Nov 19	Nov 20	2	7.3	Not started	Task			
7.5	Draft the final report and the reasoning behind each design choice	Devam, Carl	Nov 19	Nov 21	3	7.3	Not started	Task			
G7	GATE Every result logged with three runs each, diagrams match the build	Michael	Nov 21	Nov 21	1	7.2, 7.4	Not started	Gate			
S5	SPRINT 5 (Jira)	All	Nov 24	Dec 5	12	G7	Not started	Sprint			
W8	WEEK 8 Freeze, rehearse, deliver	All	Nov 24	Dec 1	8	G7	Not started	Week	Nov 17	Nov 21	10
8.1	Freeze the configuration and rerun the full Appendix F test plan one last time	All	Nov 24	Nov 25	2	G7	Not started	Task			
8.X	*Thanksgiving, no work planned*		*Nov 26*	*Nov 26*	*1*			*Blackout*			
8.2	Finish the report, including known limits and the root cause of any test that failed	Devam	Nov 27	Nov 28	2	8.1	Not started	Task			
8.3	Record the video demo with all four members narrating	All	Nov 27	Nov 29	3	8.1	Not started	Task			
8.4	Build the slides and rehearse the full presentation twice	All	Nov 29	Nov 30	2	8.3	Not started	Task			
8.5	Practice Q and A: each member answers questions on a zone they did not build	Carl	Dec 1	Dec 1	1	8.4	Not started	Task			
G8	GATE FINAL DELIVERY: package submitted, all four ready for any question	Carl	Dec 1	Dec 1	1	8.2, 8.5	Not started	Gate			
BUF	*Buffer: spare days between final delivery and the course deadline*	*All*	*Dec 2*	*Dec 4*	*3*	*G8*		*Reserve*			
END	Course deadline		Dec 5	Dec 5	1			Deadline			
MTG	*Weekly team meeting: two hours minimum, all four present, run by Carl*	*All*	*Sep 29*	*Dec 1*	*64*		*Ongoing*	*Recurring*			

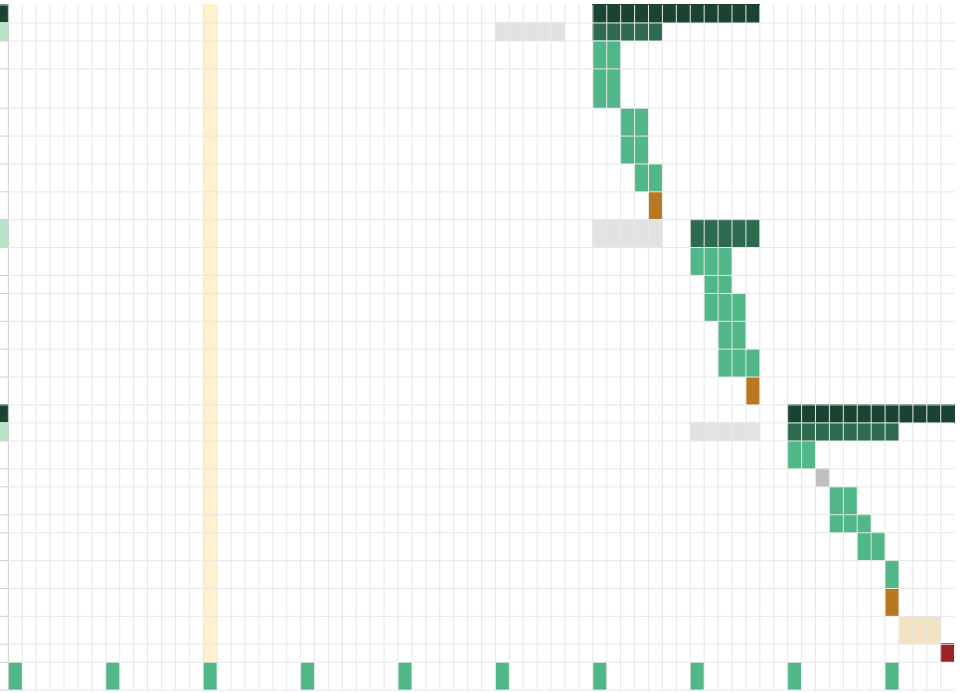

How to read this

- Jira sprint window
- Scope week, current forecast
- Scope week, original baseline (where it was supposed to be)
- Task
- Task complete
- Gate: the team does not move on until it passes
- Buffer
- Blackout
- Course deadline
- Today

PM notes

Why Week 2 moved. Thompson's design review was planned for Oct 10. He acknowledged the scope on Oct 8, which left no time to review a design that same week. The plan and matrix go to him Oct 15, the review is targeted for Oct 17, and the build weeks after it move back one week.

Why we did not cram to catch up. The scope says a missed gate means the PM replans instead of rushing. Every later week keeps its full five days. The lost week comes out of the buffer before the course deadline, which drops from two weeks to three days.

How Week 3 still started on time. While the review is pending, the team places and cables every device and writes each config as a text file. Nothing is loaded onto a device until Thompson approves, so the gate holds and no time is wasted.

Backup plan if we need more room. Start the Week 7 paperwork (config export, diagrams) during Week 6 testing, since those do not depend on the test results.

Thanksgiving lands in Week 8, so the report and video start the day after and practice Q and A moves to Dec 1.

Why this order. If ACL rules go on top of broken routing, there is no way to tell which one caused a problem. So routing is proven first, then the rules, then hardening.

Every bar, duration and slip number is calculated from the dates. Change a date and the chart redraws itself.

What each week delivers and who it is for

Jira sprint	Scope week	Window	User story	Done when (gate)	Owner
1	**1**	Sep 29 to Oct 3	As the sponsor, I want the team working from one topology and one naming scheme so every config and diagram reads the same.	Topology and naming agreed, all four committing	Carl
1 into 2	**2**	Oct 6 to Oct 17	As the network engineer, I want an addressing plan that summarizes cleanly at each area border so routing tables stay small and readable.	Sponsor approves plan and policy matrix	Jaden
2	**3**	Oct 20 to Oct 24	As a user in any zone, I need to reach the rest of my own zone before anyone starts restricting traffic between zones.	Adjacencies FULL, intra zone reachability proven	Carl
3	**4**	Oct 27 to Oct 31	As the security officer, I want contractors and guests kept out of every internal resource while each department keeps the access it actually needs.	Every rule behaves as written, hit counters prove it	Jaden
3	**5**	Nov 3 to Nov 7	As an auditor, I want proof for every zone pair in both directions, not just the easy ones.	Full matrix evidenced, cross training done	Michael
4	**6**	Nov 10 to Nov 14	As the operations lead, I need the policy to hold after a link fails and OSPF reconverges, and I need routing updates authenticated.	Hardening applied, every failure scenario passed	Devam, Carl
4	**7**	Nov 17 to Nov 21	As the professor, I want repeatable results: three timed runs, exported configs and diagrams that match the build.	Matrices complete, diagrams synchronized	Michael, Devam
5	**8**	Nov 24 to Dec 1	As the audience, I want any one of the four presenters to explain any zone, not just their own.	Package submitted, team rehearsed twice	All

Roles, zone ownership and effort (Appendix C of the signed scope)

Member	Role	Owns	Tasks assigned	Hrs per week	Weeks	Planned hours
Carl Edouard	Project Manager and backbone owner	Management zone, OSPFv2 backbone and its authentication, sponsor relationship, gate checklist	21	12	8	96
Jaden Torres	Zone policy and addressing lead	Engineering zone, VLSM plan, directional policy matrix, ACL design for every boundary	18	12	8	96
Michael Pietrewicz	Verification and testing lead	Corporate and Contractor/Guest zones, verification and failure test matrices, evidence archive	18	12	8	96
Devam Patel	Security, documentation and diagram lead	Server/DMZ zone and its service, device hardening, both diagrams, final report, exported configs	18	12	8	96
Team total						**384**

Hours follow the signed scope: 4 members, 12 hours a week, 8 weeks.

Tasks assigned counts every task that names the member, including tasks owned by All.

Everyone configures devices and must be able to explain any zone at the final presentation. Ownership means accountability, not exclusive access.
